


PICTURE

Steel Structure

● Light Gauge Steel Frame




● Steel Columns And Beams(.painted)

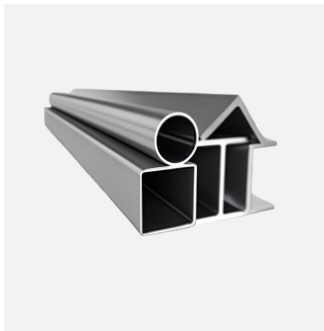


Roofing

● TPO Waterproof Membrane

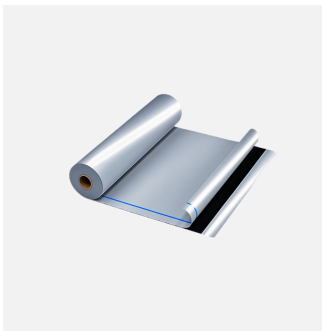

● OSB Board

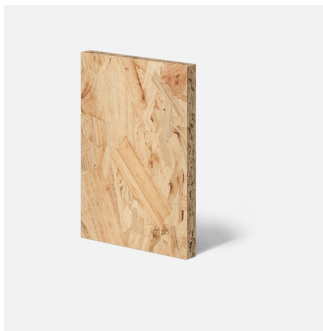

● Rockwool Insulation




● Steel Batten




● OSB Board



● Wood Cladding

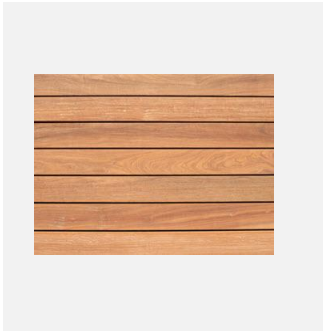

● OSB Board

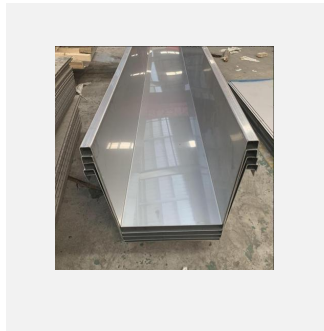

● Downspouts



PICTURE

Exterior Wall

● Fiber Cement Cladding Board



● Steel Batten



● Building Paper



● Integrated Wall Panel



● OSB Board



● Rockwool Insulation



Interior Finishes

● Plywood Board(with UV coating)



● Ceramic Tile(Economic)



● SPC Flooring



● Skirting




Windows and Doors


● Aluminum Alloy Glass Sliding Door



● Glass Window

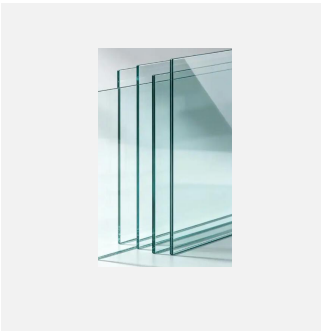

● Barn door

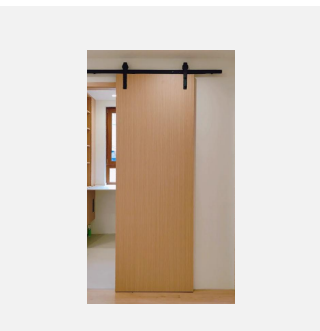

PICTURE

Bathroom And Kitchen

● Stainless Kitchen Sink



● Faucet for Kitchen Sink



● Shower Screen



● ShowerFaucet



● Toilet



● Vanity



● Faucet for Vanity



Electric

● Down Spotlight





PLATINUM
Since 2008

Project No: Q26741

I. PROJECT BRIEF

- **Project Name:** Canadian Mirror House
- **Project Address:** Canada
- **Sales Contact:** JCK
- **Customer:**

Building Overview

Building Area:	48	m2
Storeys:	1	

Scope of Work

• Building Structure	✓ Steel Structure
• Interior Space	✓ Kitchen ✓ Bathroom
• Building Enclosure	✓ Roofing ✓ Exterior Walls
• Building Construction	✓ Door & Window ✓ Floor & Ceiling
• Other	✓ Plumbing ✓ Electric

Allowed Maximum Load Capacity (Check with us if your request varies.)

Roof Live Load: 2.0KN/m ²	Floor Live Load: 2.0KN/m ²
Snow Load: 2.0KN/m ²	Wind Load: 35m/s
Seismic: 0.06g	Design Life: 50 Years

II. PROJECT PLAN



III. QUOTATION SUMMARY

Price in: USD Rate: 6.7

Seq.	Project	Area(m2)	Qty	Total(m2)	Unit Price(USD)	Total(USD)
A. PRODUCT COST						
1	STEEL STRUCTURE	48.0	1	48.0	11,609.61	11,609.61
2	ROOFING	48.0	1	48.0	3,041.95	3,041.95
3	EXTERIOR WALL	48.0	1	48.0	2,006.79	2,006.79
4	INTERIOR WALL	48.0	1	48.0	261.74	261.74
5	FLOOR AND CEILING	48.0	1	48.0	957.41	957.41
6	INTERIOR FINISHES	48.0	1	48.0	1,761.08	1,761.08
7	WINDOWS AND DOORS	48.0	1	48.0	14,288.96	14,288.96
8	KITCHEN AND BATHROOM	48.0	1	48.0	5,478.09	5,478.09
9	PLUMBING AND ELECTRIC	48.0	1	48.0	1,289.55	1,289.55
10	WHOLE-HOUSE SYSTEM INTEGRATION & TECHNICAL COMPLIANCE FEE	48.0	1	48.0	2,848.66	2,848.66
B. PREFABRICATION & SERVICE COST						
11	PREFABRICATION & SERVICE COST		1		309.59	309.59
C. LOGISTICS COST						
12	LOGISTICS COST		1		1,438.81	1,438.81
Total Quotation (FOB):						45,292.23

* Port handling charges (if applicable) will be charged per actual amount. Excess refunded, shortfall supplemented.
* Supply Scope: All materials and components are subject to the final BOQ and approved drawings.

BUILDING SYSTEM DESCRIPTION

External Wall System	Roof System	Floor System
Wood Cladding	TPO Waterproof Membrane	Spc Vinyl Flooring
Steel Batten	OSB Board	OSB Board
Building Paper	90mm Rockwool Insulation	90mm Rockwool Insulation
OSB Board	Light Gauge Steel Framing System	Steel Floor Structure
90mm Rockwool Insulation	Steel Batten	Wood Cladding
Light Gauge Steel Framing System	OSB Board	
Plywood Board(with UV coating)	Plywood Board(with UV coating)	

REMARKS

1. Price Basis:	This quotation is based on FOB Shanghai, China terms and priced in CNY (RMB). USD conversion (if required) shall be based on the agreed exchange rate at the time of contract confirmation.
2. Project Pricing Basis	This quotation is based on the current project scope, approved layout, and specified building systems.
3. Area & Quantity Basis	Quoted quantities and pricing are based on the actual fabrication area and final approved shop drawing dimensions. Material quantities include estimated production wastage.
4. Scope of Supply	Only the items clearly listed in this BOQ are included in the supply scope. Any items not listed shall be considered excluded.
5. Material & Drawing Confirmation	Final material specifications, dimensions, and quantities shall be subject to confirmed shop drawings before production. Any revisions after confirmation may affect pricing and delivery schedule.
6. Design & Engineering Service	Structural design and shop drawings are included in this quotation. Up to two revisions are included. Additional revisions or major design changes may incur extra charges.
7. Production Lead Time	Estimated production time is 45–60 days after receipt of deposit and final shop drawing confirmation.
8. Payment Terms	Standard payment terms: 50% deposit by T/T upon order confirmation 50% balance by T/T before shipment
9. Installation & Technical Support	On-site installation is not included in this quotation. Installation guidance and technical support can be provided upon request.
10. Freight & Logistics	Ocean freight, destination charges, local transportation, foundation works, permit-related costs, and on-site installation are excluded unless otherwise stated. Shipping costs can be quoted separately upon request.
11. Packing & Loading	Standard factory packing and container loading are included for all prefabricated components unless otherwise stated.
12. Finishing Works Clarification	Only the paint and putty works specifically listed in this BOQ are included. Any additional finishing materials or decorative works are excluded.
13. Product Images & Reference Materials	All images shown in this quotation are for reference only. Final specifications and product details shall be subject to the signed contract and approved shop drawings.
14. Technical Standards	Materials and systems are based on PLATINUM standard specifications unless otherwise stated in writing.
15. Quotation Validity	This quotation is valid for 15 days from the date of issue.

WHY CHOOSE PLATINUM

✓ 18+ Years Experience:	Serving global building projects since 2008.
✓ Integrated Building Solutions:	From structural systems to complete building material packages.
✓ Factory-Based Production:	Precision manufacturing with efficient prefabrication.
✓ Engineering Support:	Shop drawings, structural solutions, and technical coordination.
✓ Global Project Experience:	Projects delivered across the USA, Australia, Europe, and other international markets.

IV. BILL OF QUANTITY

NO.	Description	Item Name	Specification	Std/Brand	Rounding QTY.	Unit	Price (CNY)	Total (CNY)
STEEL STRUCTURE								¥77,784.36
1	Steel Structure	Steel Columns And Beams(Q235, painted)	Grade: GB-Q235, Yield Strength ≥235 MPa, including factory welding and sandblast(Sa2.5), painted with Epoxy Zinc Rich paint		48.00	m2	1,263.31	60,639.00
2	Steel Structure	Light Gauge Steel Frame (G350, Z275)	Cold formed steel in 'C' sections, wall studs spacing @ 600/610 nominally Grade: SGH440, yield strength ≥335MPa Coating: Galvanized Z275		48.00	m2	303.20	14,553.36
3	Steel Structure	Accessory for LGS Frame	Including Bolts, Screws, Holddowns, Clips, Angles, Bracing Sets		48.00	m2	54.00	2,592.00
ROOFING								¥20,381.07
4	Roofing	TPO Waterproof Membrane	t=1.2mm, Reinforced, including glue		55.20	m2	54.00	2,980.80
5	Roofing	OSB Board	15mm*1220*2440, structural board		53.58	m2	48.79	2,614.39
6	Roofing	Rockwool Insulation	150mm, 120kg/m3		50.40	m2	65.30	3,291.12
7	Roofing	Steel Batten	h=22mm, t=0.8mm		84.00	m	7.44	624.96
8	Roofing	OSB Board	8mm*1220*2440, structural board		53.58	m2	33.38	1,788.79

IV. BILL OF QUANTITY

NO.	Description	Item Name	Specification	Std/Brand	Rounding QTY.	Unit	Price (CNY)	Total (CNY)
9	Roofing	Wood Cladding	15mm*125*4000, vertical, not painted		50.50	m2		
10	Roofing	Gutter	Stainless Steel Gutter, t=1.0mm, W=200mm		27.00	m	315.00	8,505.00
11	Roofing	Downspouts	PVC-75*2.3, including clips 4m/each		16.00	m	36.00	576.00
EXTERIOR WALL								¥13,445.49
12	Exterior Wall	Wood Cladding	15mm*125*4000, vertical, not painted		72.00	m2		
13	Exterior Wall	Steel Batten	h=22mm, t=0.8mm		120.00	m	7.44	892.80
14	Exterior Wall	Building Paper	DuPont Tyvek® 150m2/roll		100.00	m2	25.74	2,574.00
15	Exterior Wall	OSB Board	12mm*1220*2440, structural board		77.40	m2	40.57	3,140.33
16	Exterior Wall	Rockwool Insulation	150mm, 120kg/m3		71.90	m2	65.30	4,695.07
17	Exterior Wall	Plywood Board(with UV coating)	12mm*1220*2440, 520kg/m3	Dry Wall	35.72	m2	60.00	2,143.30
INTERIOR WALL								¥1,753.65

IV. BILL OF QUANTITY



NO.	Description	Item Name	Specification	Std/Brand	Rounding QTY.	Unit	Price (CNY)	Total (CNY)
18	Interior Wall	Plywood Board(with UV coating)	12mm*1220*2440, 520kg/m3	Dry Wall	8.93	m2	60.00	535.82
19	Interior Wall	Rockwool Insulation	90mm, 120kg/m3		15.50	m2	44.00	682.00
20	Interior Wall	Plywood Board(with UV coating)	12mm*1220*2440, 520kg/m3	Dry Wall	8.93	m2	60.00	535.82
FLOOR AND CEILING								¥6,414.63
21	Floor	OSB Board	18mm*1220*2440, structural board	Above Floor	53.58	m2	58.29	3,123.51
22	Floor	Rockwool Insulation	150mm, 120kg/m3	Ceiling	50.40	m2	65.30	3,291.12
23	Floor	Wood Cladding	15mm*125*4000, vertical, not painted		72.00	m2		
INTERIOR FINISHES								¥11,799.26
24	Interior Finishes	SPC Flooring	4.0*180*1220mm including 2mm softwood underlay	Dry Floor	47.65	m2	98.00	4,670.01
25	Interior Finishes	Ceramic Tile(Economic)	8mm matt tile	Wet Wall	19.08	m2	82.40	1,572.19
26	Interior Finishes	Fibre Cement Board	12mm*1220*2440 (medium density, 1.2-1.5g/cm3)		20.84	m2	36.87	768.26

IV. BILL OF QUANTITY

NO.	Description	Item Name	Specification	Std/Brand	Rounding QTY.	Unit	Price (CNY)	Total (CNY)
27	Interior Finishes	Ceramic Tile(Economic)	8mm matt tile, non-slip	Wet Floor	3	m2	100.80	326.59
28	Interior Finishes	WPC Deck Flooring	25*140	Wet Floor	19	m2	198.00	3,742.20
29	Interior Finishes	Accessory for Decorative baseboards, etc.	Including Bolts, Screws		48.00	m2	15.00	720.00
WINDOWS AND DOORS								¥95,736.00
30	Doors	Aluminum Alloy Glass Sliding Door	5mm+9Argon+5mm+1.14PVB+5mm tempered clear glass	W6000xH2400	1	set	33,264.00	33,264.00
31	Doors	Barn door	MDF W800 x H2100 include common lock & hardware		1	set	1,560.00	1,560.00
32	Windows	Glass Window	1. Material: 109 Series Primary thermal break aluminum casement window 2. Thickness: 1.8mm 3. Wall thickness: 4.3"/109mm 4. Triple glazed Temered glass: 6mm/LOW-E+12A+6mm/Low-e+12A+6mm 5. No hardwares 6. dual layered Low-e glass + Argon gas 7. MOQ≥1m² per window 8. Fixed		32.40	m2	1,880.00	60,912.00
KITCHEN AND BATHROOM								¥36,703.18
33	Kitchen	Stainless Kitchen Sink	Double Sink, Stainless Steel		1	set	764.50	764.50
34	Kitchen	Faucet for Kitchen Sink	Hot-cold water mixer, American Standard	UPC	1	set	715.00	715.00

IV. BILL OF QUANTITY

NO.	Description	Item Name	Specification	Std/Brand	Rounding QTY.	Unit	Price (CNY)	Total (CNY)
35	Kitchen	Full Height Cabinet	H=2400, Particle Board, Single Side Lacquered		1.80	m	4,537.50	8,167.50
36	Kitchen	Central Island	Particle Board, Single Side Lacquered		2.70	m	5,175.00	13,972.50
37	Kitchen	Counter Top of Cabinet	Artificial Marble		3.50	m	1,650.00	5,775.00
38	Bathroom	Shower Screen (8mm toughened glass)	W500.xH2000 toughened glass fixed with chrome;		1	set	900.00	900.00
39	Bathroom	Shower faucet	wall-mounted thermostatic shower mixer with flexible hose and hand shower, American Standard	UPC	1	set	2,145.00	2,145.00
40	Bathroom	Wall Hung Toilet	Ceramic Toilet With Consealed Flushing System, American Standard	UPC	1	set	1,760.00	1,760.00
41	Bathroom	Vanity	W500*H500*D250,excluding faucet		1	set	1,680.00	1,680.00
42	Bathroom	Faucet for Vanity	Hot-cold water mixer, American Standard	UPC	1	set	823.68	823.68
PLUMBING AND ELECTRIC								¥8,640.00
43	Plumbing & Electric	Water Supply Pipe and Accessory	PEX pipe, American Standard	UPC	1	set	1,836.00	1,836.00
44	Plumbing & Electric	Sewage Pipe and Accessory	PVC pipe, American Standard	UPC	1	set	1,224.00	1,224.00

IV. BILL OF QUANTITY



NO.	Description	Item Name	Specification	Std/Brand	Rounding QTY.	Unit	Price (CNY)	Total (CNY)
45	Plumbing & Electric	Down Spotlight	LED	UL Listed	12	set	75.00	900.00
46	Plumbing & Electric	Electrical Components	American Standard, including Electric Wire, Sockets, Conduit, Switches, Outlets excluding Electric Boxex, Breakers	UL Listed	1	set	4,680.00	4,680.00
WHOLE-HOUSE SYSTEM INTEGRATION & TECHNICAL COMPLIANCE FEE								¥19,086.03
47	Service	WHOLE-HOUSE SYSTEM INTEGRATION & TECHNICAL COMPLIANCE FEE			1	set	19,086.03	19,086.03
PREFABRICATION AND SERVICE								¥2,074.28
48	Other Fees	Assembly of LGS Wall Panels in Factory	Steel Wall Frame Pre-assembled in Factory		131.70	m2	15.75	2,074.28
LOGISTICS								¥9,640.00
49	Service	Packing & Loading for LGS House	Packing & Loading in Factory for prefab house		1.00	set	2,500.00	2,500.00
50	FOB Fees	Estimated one 40HQ to load, the final according to the actual	Trailer, customs declaration, etc., to be subject to actual costs		1	set	7,140.00	7,140.00
Grand Total(CNY)								303,457.95
Exchange Rate: 6.7					Grand Total(USD)		45,292.23	
